

FLOMSIKRING GIVRA

OVERORDNET HOVEDFRAMDRIFTSPLAN

ID	Aktivitet	Varighet (arb.dager)	Start	2020 June					2020 July					2020 August					2020 September									
				01	06	11	16	21	26	01	06	11	16	21	26	31	05	10	15	20	25	30	04	09	14	19	24	
1	GIVRA	494 days	Tue 19-10-01																									
2	DEL 1 (Skåbuvn til oppstrøms grensesnitt)	412 days	Tue 19-10-01																									
42	DEL 3 (Sundheimvn og ned til Lågen)	412 days	Tue 19-10-01																									
43	Prosjektering og kontrahering Del 3	225 days	Tue 19-10-01																									
44	Kostnadsoverslag alternative løsninger	5 days	Tue 19-10-01																									
45	Behandling NVE alternative løsninger	15 days	Tue 19-11-12																									
46	Beslutning åpen eller lukket løsning	0 days	Mon 19-12-09																									
47	Geoteknisk undersøkelse og rapport	22 days	Thu 19-10-31																									
48	Beslutning inntaksløsning	0 days	Tue 20-02-18																									
49	Låse inntakskonstruksjon, kulvertlinje og veglinje	14 days	Tue 20-02-18																									
50	Konstruksjoner og erosjonssikring	56 days	Mon 20-03-09																									
51	Prosjektering	40 days	Mon 20-03-09																									
52	Tegninger til gjennomsyn byggherre	0 days	Mon 20-05-18																									
53	Beskrivelse til gjennomsyn byggherre	0 days	Mon 20-06-08	◆ 06-08																								
54	VA	56 days	Mon 20-03-09																									
55	Prosjektering	50 days	Mon 20-03-09																									
56	Tegninger til gjennomsyn byggherre	0 days	Wed 20-05-27	-27																								
57	Beskrivelse til gjennomsyn byggherre	0 days	Mon 20-06-08	◆ 06-08																								
58	Veg	56 days	Mon 20-03-09																									
59	Prosjektering	45 days	Mon 20-03-09																									
60	Tegninger til gjennomsyn byggherre	0 days	Tue 20-05-19																									
61	Beskrivelse til gjennomsyn byggherre	0 days	Mon 20-06-08	◆ 06-08																								
62	Generelle deler	115 days	Tue 19-12-10																									
65	Kontrahering	48 days	Thu 20-06-25																									
66	Utlysing	0 days	Thu 20-06-25	◆ 06-25																								
67	Tilbudsregning	25 days	Thu 20-06-25																									
68	Evaluering og evt forhandlinger	15 days	Thu 20-08-27																									
69	Tildeling og karenstid	8 days	Thu 20-09-17																									
70	Kontraktsinngåelse	0 days	Mon 20-09-28																									
71	Reguleringsplan Del 3	52 days	Fri 20-03-27																									
77	Fellesaktiviteter for Del 3	127 days	Mon 20-03-09																									
78	Nabovarsling	15 days	Tue 20-06-23																									
79	Byggesøknad	15 days	Tue 20-09-22																									
80	Byggetillatelse	0 days	Mon 20-10-12																									
81	Grunneieravtaler	100 days	Mon 20-03-09																									
82	Anleggsperiode Del 3	175 days	Thu 20-10-15																									
85	DEL 2 (Skåbuvn - Sundheimvn)	438 days	Wed 19-12-18																									


Prosjekt: Flomsikring Givra
Rev.dato: 2020-06-10

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

FLOMSIKRING GIVRA

OVERORDNET HOVEDFRAMDRIFTSPLAN

2020 October 29 04 09 14 19 24 29	2020 November 03 08 13 18 23 28	2020 December 03 08 13 18 23 28	2021 January 02 07 12 17 22 27	2021 February 01 06 11 16 21 26	2021 March 03 08 13 18 23 28	2021 April 02 07 12 17 22
--	--	--	---	--	---	--------------------------------------

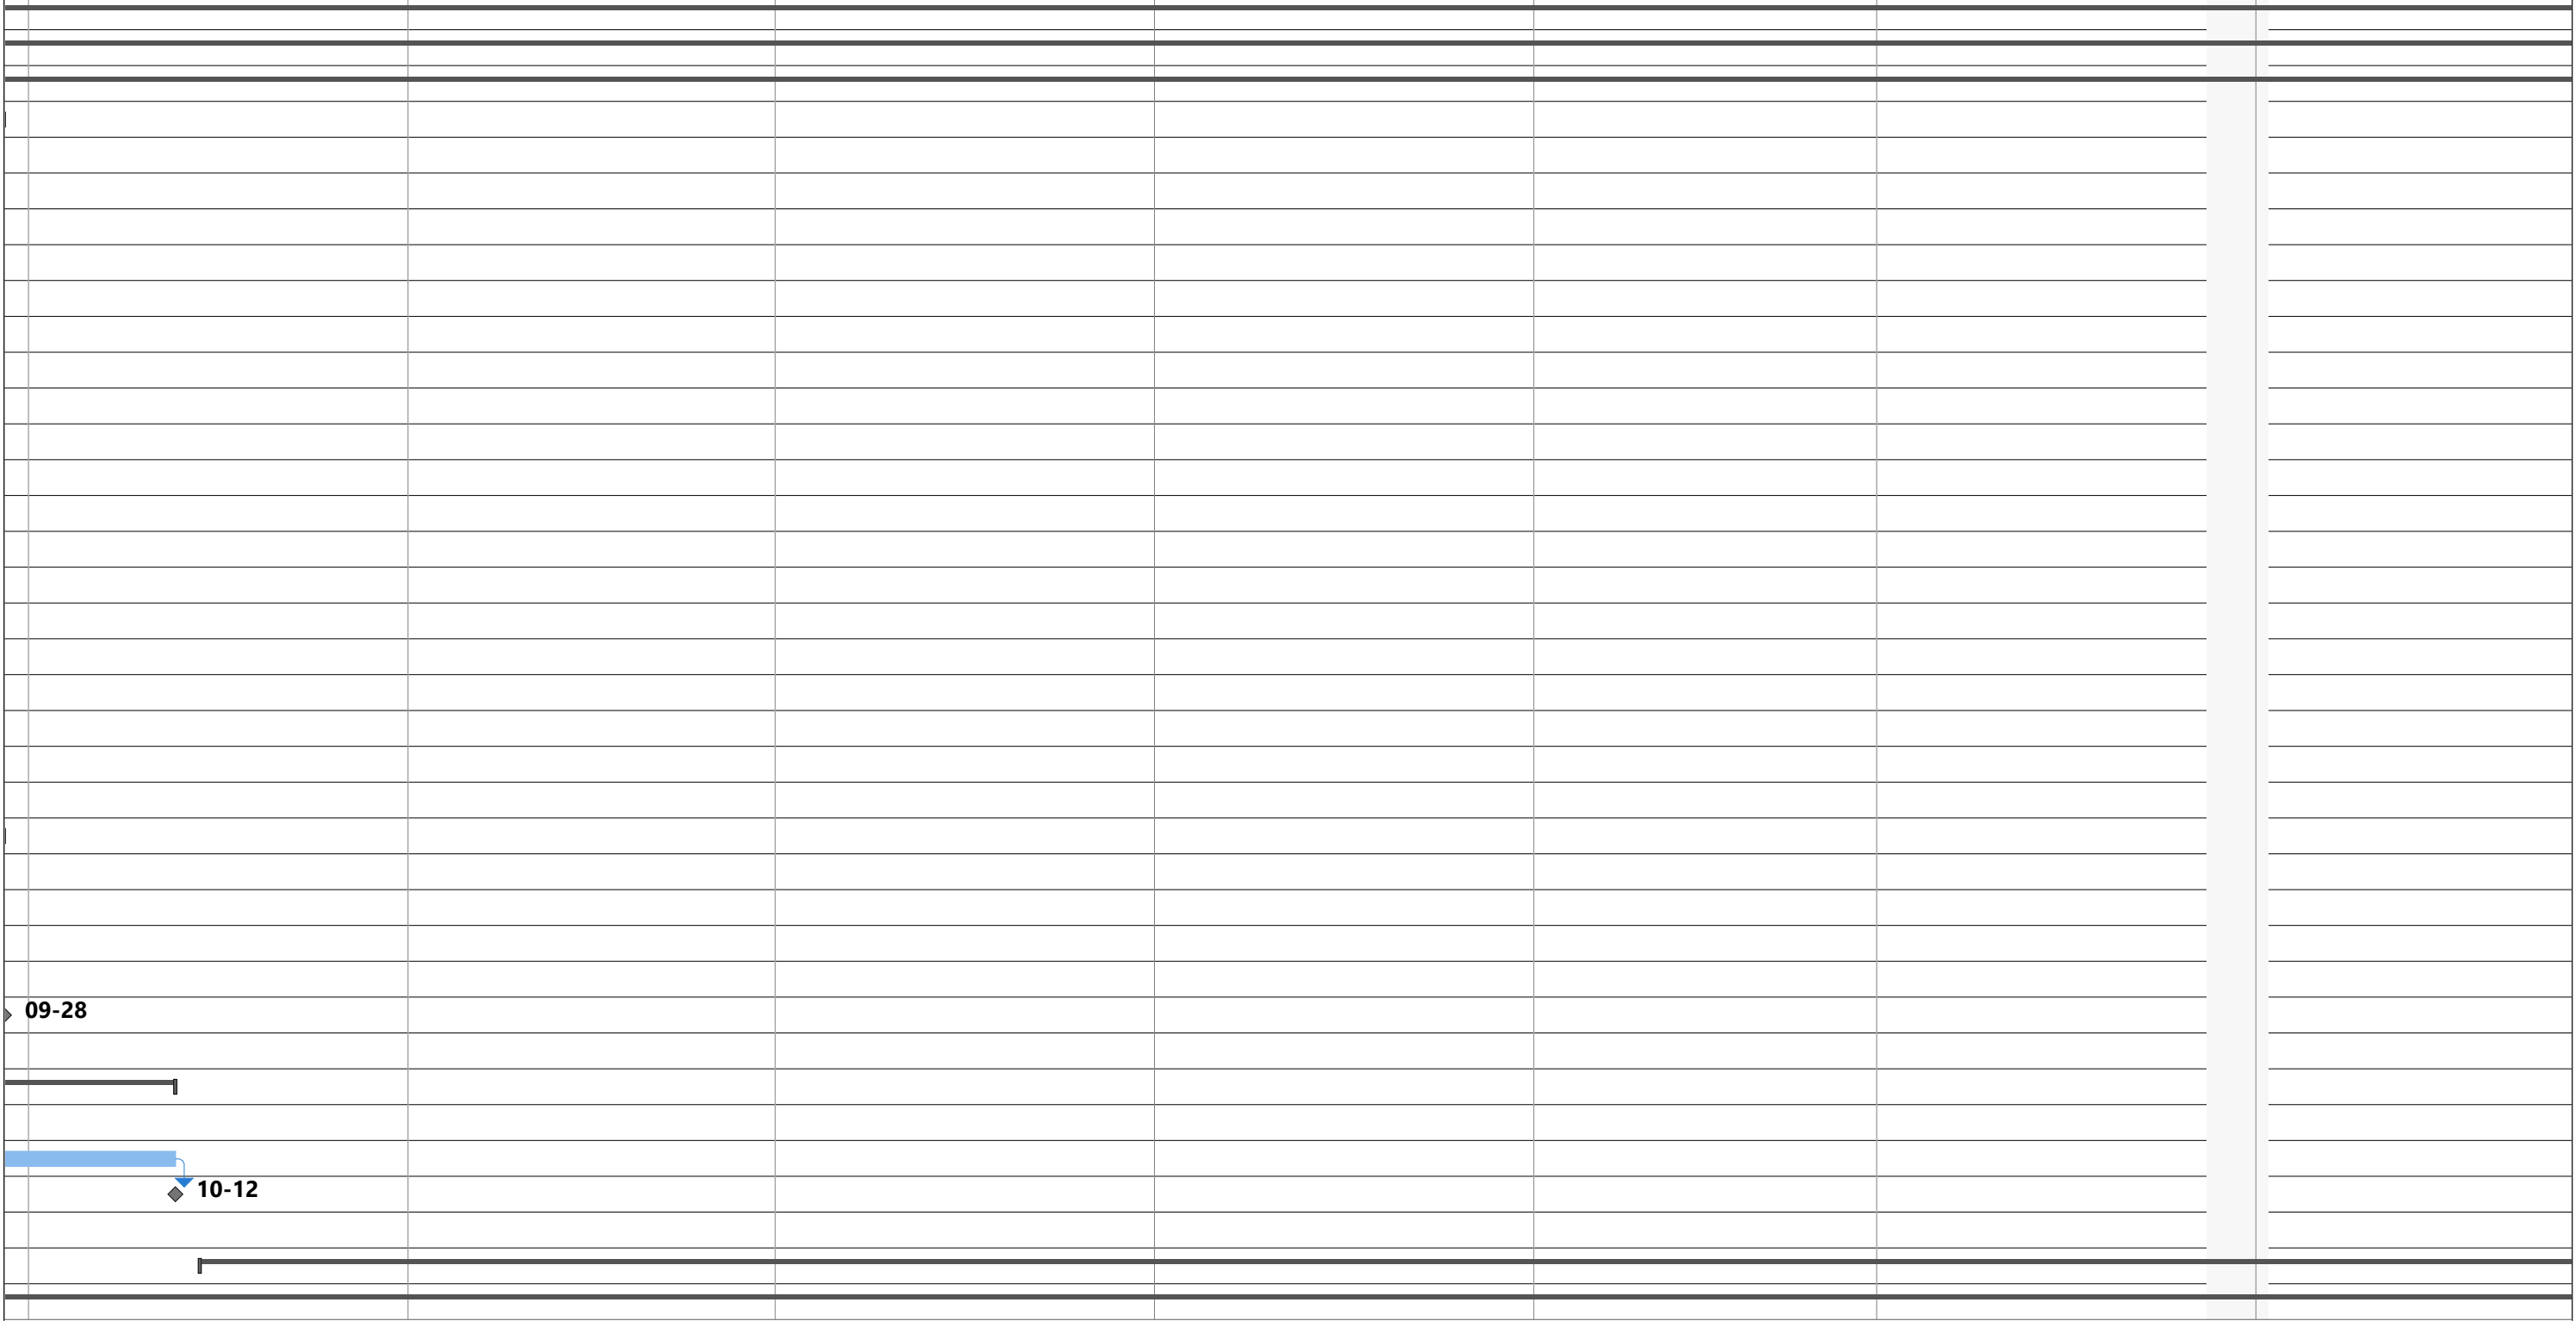

► 09-28


◆ 10-12

Prosjekt: Flomsikring Givra
Rev.dato: 2020-06-10

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

FLOMSIKRING GIVRA

OVERORDNET HOVEDFRAMDRIFTSPLAN

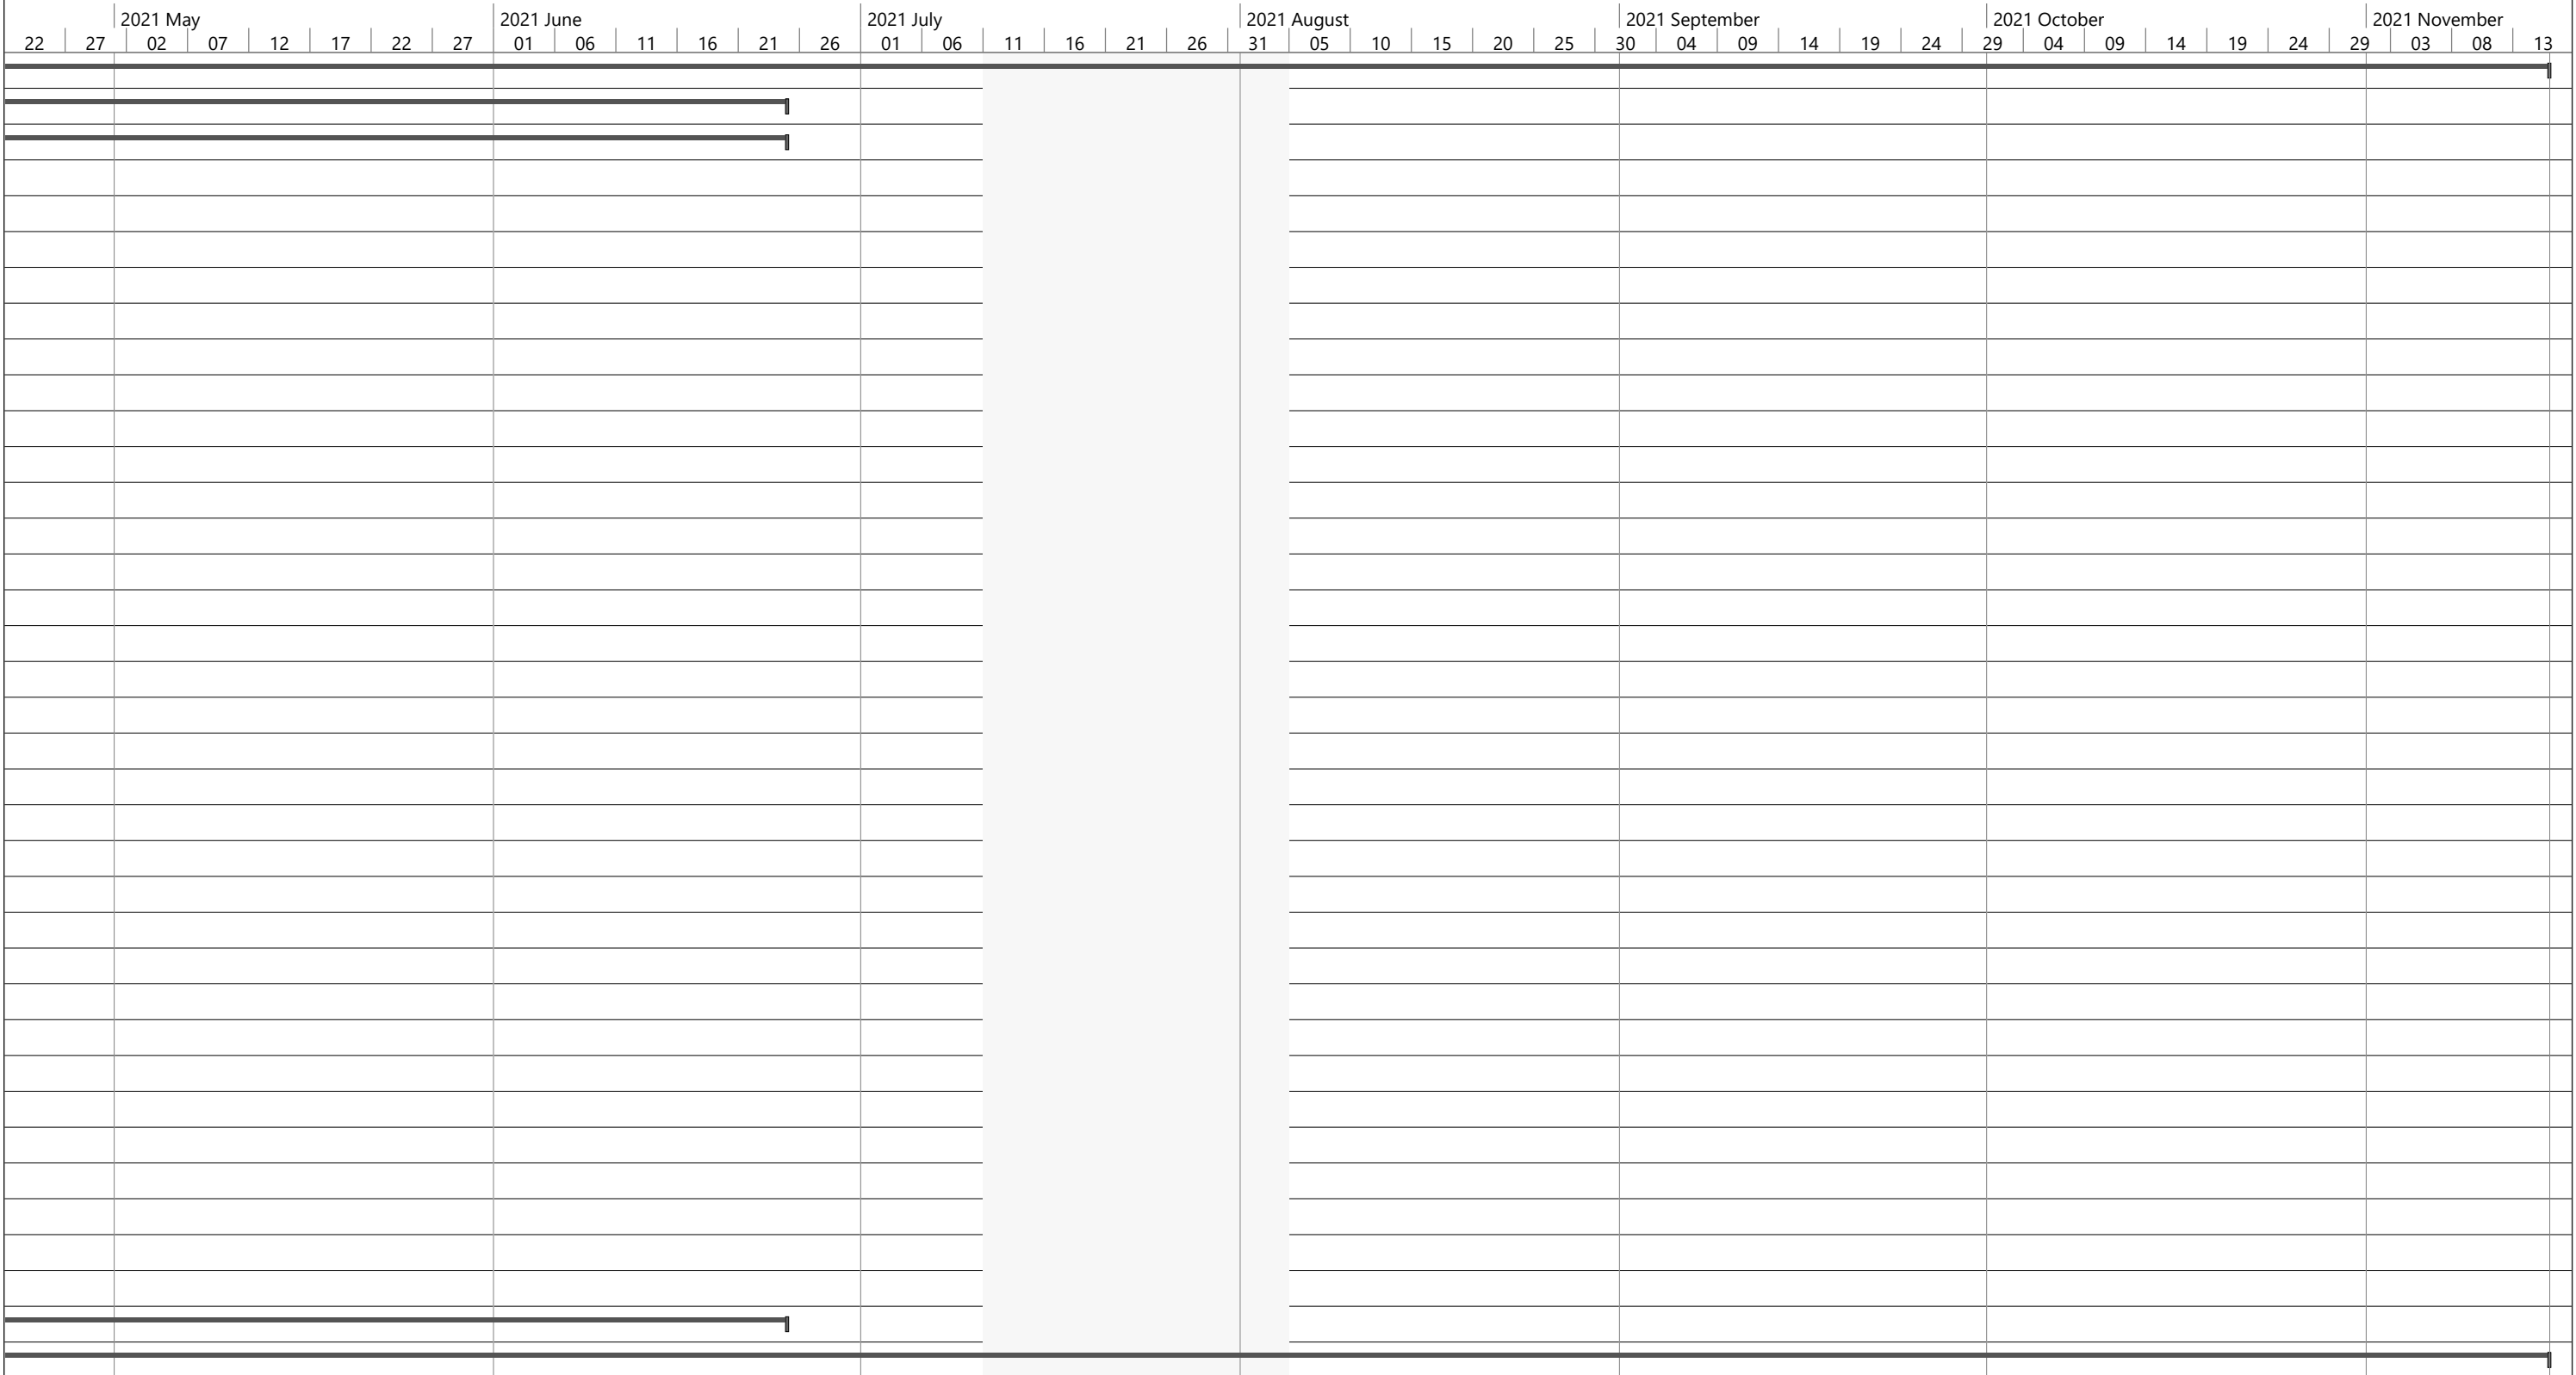

Prosjekt: Flomsikring Givra
Rev.dato: 2020-06-10

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

FLOMSIKRING GIVRA

OVERORDNET HOVEDFRAMDRIFTSPLAN

2021 December				2022 January				2022 February				2022 March				2022 April				2022 May				2022 June																											
13	18	23	28	03	08	13	18	23	28	02	07	12	17	22	27	01	06	11	16	21	26	03	08	13	18	23	28	02	07	12	17	22	27	02	07	12	17	22	27	01	06										

Prosjekt: Flomsikring Givra
Rev.dato: 2020-06-10

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
